

EQUIPMENT SUBMITTAL

Static UPS

Project: Meridian Data Centre Campus - Phase 1

Reference Section: 26 33 53

Package ID: SUB-263353-01-R1

Revision: R1

Reviewed Spec Revision: Rev 2024


Date: 01-01-2025

ACTIVE

Rev	Date	Description
R1	01-01-2025	Initial / Updated Submittal

Technical Parameters

Parameter	Claimed Value
Battery Chemistry	VRLA
Battery Runtime	10 min
UPS Module Capacity	1200 kW
Cooling Airflow Configuration	Rear-exhaust
Efficiency at 100% Load	96.2%
Efficiency at 50% Load	96.2%
Efficiency at 75% Load	96%
Enclosure Paint Finish	RAL 9005
Input Harmonic Distortion	5.2%
Input Voltage	415 V
Output Voltage	415 V
Inverter Overload Capacity	125% for 5 minutes
Parallel Redundancy Configuration	N+1
Power Factor	1

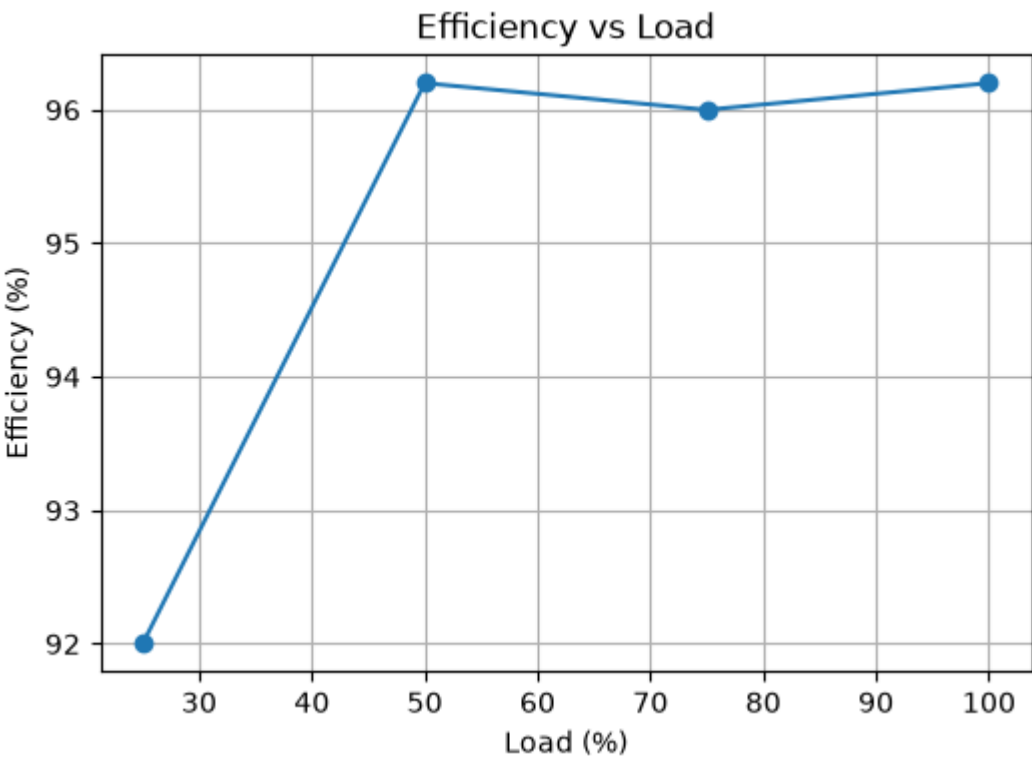

Clause ID	Requirement Summary	Response
26 33 53 Part 2.2.1.D	Input total harmonic current distortion (THDi) shall not exceed 5.0% at full rated load without exte...	Comply
26 33 53 Part 2.3.4	UPS double-conversion efficiency shall be a minimum of 96.0% at each of the 50%, 75%, and 100% load ...	Comply
26 33 53 Part 2.3.4	UPS double-conversion efficiency shall be a minimum of 96.0% at each of the 50%, 75%, and 100% load ...	Comply
26 33 53 Part 2.3.4	UPS double-conversion efficiency shall be a minimum of 96.0% at each of the 50%, 75%, and 100% load ...	Comply
26 33 53 Part 2.2.8	The static bypass switch transfer time shall not exceed 4 milliseconds for any transfer between inve...	Comply
26 33 53 Part 2.2.5.A	UPS module shall sustain 125% of rated load for a minimum of 10 minutes continuously without transfe...	Comply
26 33 53 Part 2.4.2	UPS module cooling airflow shall be configured for front-inlet and top-exhaust to support hot aisle/...	Comply
26 33 53 Part 2.4.5.C	UPS module enclosure paint finish shall be RAL 7035 (Light Grey) polyester powder coating, minimum 6...	Comply
26 33 53 Part 2.2.1.A	Each UPS module shall have a minimum continuous output power rating of 1200 kW at unity power factor...	Comply
26 33 53 Part 2.2.1.B	UPS module output power factor shall be unity (1.0 PF) at full rated load. No derating for power fac...	Comply

Clause ID	Requirement Summary	Response
26 33 53 Part 1.4.1.C	UPS equipment shall be tested and certified in accordance with IEC 62040-3 (Method of Specifying the...	IEC 62040-3
26 33 53 Part 1.3.1	The Contractor shall submit the equipment submittal package referencing the current active project s...	Comply

CERTIFICATE OF COMPLIANCE

This certifies that the equipment complies with standard testing requirements.

Issued by: Third Party Testing Laboratory
