

# EQUIPMENT SUBMITTAL TRANSMITTAL

REVISE AND RESUBMIT

|                 |                                      |               |                |
|-----------------|--------------------------------------|---------------|----------------|
| Transmittal No: |                                      | Date:         |                |
| Project:        | Meridian Data Centre Campus, Phase 1 | Spec Section: | 26 33 53       |
| Vendor:         | VoltEdge Power Systems               | Revision:     |                |
| Status:         | FOR REVIEW                           | EPC Lead:     | YOU Electrical |

## Submittal Item Description

We submit for engineering review and approval the product datasheet, compliance matrix, and test certifications for the following equipment:

| Model Number    | Description                                         | Qty | Manufacturer           |
|-----------------|-----------------------------------------------------|-----|------------------------|
| VoltEdge BC-200 | VoltEdge BC-200 High-Rate VRLA Battery Cabinet Rack | 24  | VoltEdge Power Systems |

## Review Comments / Action Taken

Engineering Review Result: REVISE AND RESUBMIT  
Comments:

- Approved with no major comments. All values check compliant.

## Product Datasheet: VoltEdge BC-200

The VoltEdge BC-200 is a matching battery cabinet rack housing high-rate Valve Regulated Lead-Acid (VRLA) batteries connected in series to provide DC back-up power to the UPS inverter during utility outages.

### Technical Parameter Specifications


| Parameter Name         | Claimed Value  | Claimed Condition       | Spec Limit    |
|------------------------|----------------|-------------------------|---------------|
| Nominal energy kwh     | 576.0 kWh      | at 10h discharge rate   | 576.0 kWh     |
| Load power factor      | 0.9            | discharge condition     | 1.0           |
| Dc bus voltage         | 400.0 V        | nominal DC bus          | 480.0 V       |
| Shelf life months      | missing months | without recharge        | 6.0 months    |
| Cabinet weight kg      | 3200.0 kg      | fully loaded            | 2800.0 kg     |
| Operating temp limit c | 20.0 C         | operating ambient limit | 25.0 C        |
| Cable entry conduit    | bottom         | installation config     | top_or_bottom |
| Lvd contactor rating   | missing        | standard coil           | continuous    |

**Notes:**

1. Cabinet houses 40 blocks of 12V 200Ah batteries in series (nominal DC bus 480VDC). Stated 576 kWh rating is the combined bank nominal capacity rating. 2. Backup autonomous runtime of 10 minutes is rated under a load power factor condition of 0.9 PF.

## Equipment Performance Curves

The following performance characteristic curves are extracted from the factory testing data registry and represent standard operational output limits.

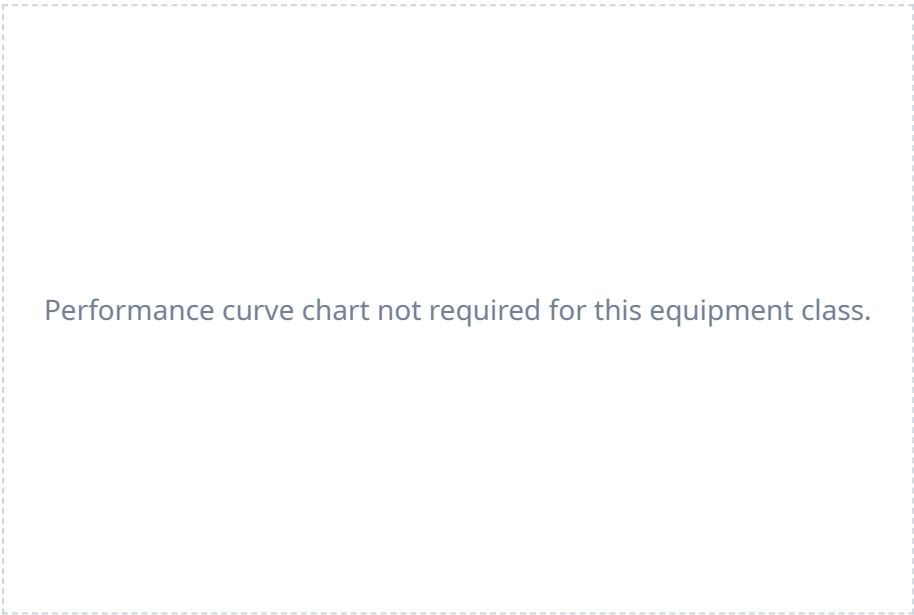

\* Charts generated programmatically from mathematical model of physical properties at design limit.

## Clause-by-Clause Conformance Statement

Below is our conformance statement indicating compliance with each clause of Section 26 33 53 of the construction specifications.

| Spec Clause                 | Parameter / Requirement | Conformance Claim | Remarks / Evidence                                                                                                                                                                                                                         |
|-----------------------------|-------------------------|-------------------|--------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| 26 33 53<br>Part<br>2.3.2.A | BAT-CAPACITY-SHORTFALL  | NC                | Non-Conformant. Vendor datasheet claims nominal capacity is 550 kWh, which when converted ( $550,000 \text{ Wh} / 480 \text{ V} = 1145.8 \text{ Ah}$ ) is below the required 1200 Ah, indicating a capacity shortfall of 54.2 Ah (4.5%).   |
| 26 33 53<br>Part<br>2.3.2.A | BAT-CAPACITY-UNIT       | C                 | Conforms. Battery capacity is quoted as '576 kWh' in the submittal. Converting this ( $576,000 \text{ Wh} / 480 \text{ V} = 1200 \text{ Ah}$ ) matches the required capacity of 1200 Ah.                                                   |
| 26 33 53<br>Part<br>2.3.2.B | BAT-PF-CONDITION        | NC                | Non-Conformant. Datasheet claims 10-minute battery runtime is rated at a load power factor of 0.9 PF. The spec requires battery runtime to be rated at a load power factor of 1.0 PF (unity), which represents a larger active power draw. |
| 26 33 53<br>Part<br>2.3.2.C | BAT-DC-BUS-VOLTAGE      | NC                | Non-Conformant. Battery cabinet DC bus voltage is listed as 400 VDC. The spec requires a 480 VDC nominal bus voltage to match the UPS inverter requirements.                                                                               |
| 26 33 53<br>Part 2.3.3      | BAT-SHELF-LIFE          | NC                | Non-Conformant. The battery shelf life (required to be $\geq 6$ months without charge) is missing from the battery cabinet specification sheet.                                                                                            |
| 26 33 53<br>Part<br>2.3.5.A | BAT-CABINET-WEIGHT      | NC                | Non-Conformant. Fully loaded battery cabinet weight is listed as 3200 kg. Spec limits the maximum floor-load weight per cabinet to 2800 kg to prevent exceeding structural slab limits.                                                    |
| 26 33 53<br>Part<br>2.3.6.B | BAT-OPERATING-TEMP      | NC                | Non-Conformant. Battery cabinet datasheet lists operating temperature of 0°C to 20°C. Spec requires full battery warranty and operating parameters to hold from 0°C to 25°C ambient.                                                       |
| 26 33 53<br>Part 2.3.8      | BAT-CABLE-ENTRY         | NC                | Non-Conformant. Battery cabinet is configured for bottom cable entry only. Spec requires dual entry (top or bottom cable entry conduits) to match overhead cable trays.                                                                    |
| 26 33 53<br>Part<br>2.3.9.C | BAT-LVD-CONTACTOR       | NC                | Non-Conformant. Low Voltage Disconnect (LVD) contactor rating is omitted from the battery cabinet component details.                                                                                                                       |

# CERTIFICATE OF CONFORMANCE

Factory Quality Assurance Department

We hereby certify that the equipment listed below has been manufactured, tested, and inspected in accordance with all active factory testing specifications and international standards.

**Equipment Model:** VoltEdge BC-200  
**Serial Numbers:** VOL-2026-2601 to 08  
**Test Standards:** IEC 62040-3, IEC 62271-200, ISO 8528-5 as applicable.  
**Quality Inspector:** Dr. H. Bose (Director of QA)  
**Date of Inspection:** January 8, 2026

Quality Inspector Signature

Plant Manager Signature
